



BRUHAT BANGALORE MAHANAGARA PALIKE

NAME OF WORK: Modified of Additional works to construction of shuttle cock Ground In Ward No 17 RR Nagar constituency

**RR Nagar Project
Measurement Sheet**

Bill No :1st And Final Bill

BRUHAT BANGALORE MAHANAGARA PALIKE							
NAME OF THE WORK: Modified of Additional works to construction of shuttle cock Ground In Ward No 17 RR Nagar constituency							
Measurement Sheet							
First and Final							
Item No:	1						
Item Name:	Dismantling Brick / Tiles Work. Dismantantling Boulders laid in wire crates including opening of crates and stacking dismantled materials. As Per Direction of Engineer Incharge						
	CHAINAGE	NO	L	B	D	QTY	REMARKS
	Land Mark		(m)	(m)	(m)		
	Door opening to Ladies Toilet	1.00	0.90	0.20	2.40	0.43	✓
	Office Entrance	1.00	4.30	0.20	3.00	2.58	✓
	Deductions						
		-1.00	1.20	0.20	2.10	-0.50	
Total Qty Work Done						2.51	cum
Qty payable in this Bill						2.51	cum

FOT S.K.S. INFRASTRUCTURES PVT. LTD.

Contractor Representative
Managing Director

R. K. Anbum
Assistant Engineer
Project -RR Nagar Division
BBMP



R. K. Anbum
Asst. Executive Engineer
Project -RR Nagar Division
BBMP

BRUHAT BANGALORE MAHANAGARA PALIKE

NAME OF THE WORK: Modified of Additional works to construction of shuttle cock
Ground In Ward No 17 RR Nagar constituency

Measurement Sheet

First and Final

Item No:

2


Item
Name:

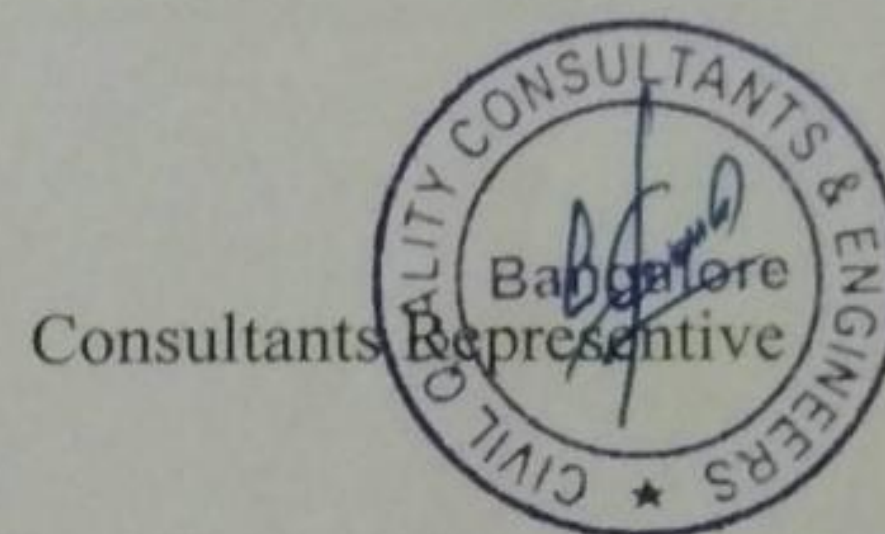
Earth work excavation for foundation of buildings, culverts water supply, sanitary line and electrical conduits either in pits or in trenches 1.5m and above in width, in Hard soil not exceeding 1.5m, in depth including dressing the bottom and sides of pits and trenches, stacking the excavated soil clear from edges of excavation with lead upto 50m, after breaking of clods complete as per specifications, As Per Direction of Engineer Incharge

CHAINAGE Land Mark	NO	L (m)	B (m)	D (m)	QTY	REMARKS
For RCC Wall	1	51.00	0.60	1.00	30.60 ✓	
	1	61.30	0.60	1.00	36.78 ✓	
Building All Round CC K	1	87.00	0.30	0.30	7.83	
	2	24.00	0.30	0.30	4.32	
	1	10.00	0.30	0.30	0.90	
For Steps	1	3.50	2.50	1.00	8.75	
	1	2.50	1.50	1.00	3.75	
	1	3.00	1.50	1.00	4.50	
For Ladies Toilet	2	12.95	1.10	2.05	58.40	
	4	4.63	1.10	2.05	41.72	
Partition Wall	1	5.75	0.90	1.50	7.76	
	5	2.20	0.90	1.50	14.85	
	1	4.63	0.90	1.50	6.25	
Compound Wall	1	13.00	0.90	1.50	17.55	
Over Burden Earth	1	3.00	4.00	1.00	12.00	
Toilet Block						
Alround	1	25.00	0.90	1.05	23.63	
Cross wall	2	6.10	0.90	1.05	11.53	
do	8	0.80	0.90	1.05	6.05	


do		1	4.30	0.90	1.05	4.06	
Flagging		1	21.60	0.75	0.15	2.43	
Steps		1	1.50	1.50	0.15	0.34	
Man hole		1	$(3.14 \times 1.8^2)/4$		2.50	6.36	
Alround		1	41.40	0.90	1.05	39.12	
Cross wall		2	14.40	0.90	1.05	27.22	
do		2x9	0.80	0.90	1.05	13.61	
Flagging		1	45.20	0.75	0.15	5.09	
Steps		1	1.50	1.50	0.15	0.34	
Man hole		1	$(3.14 \times 1.8^2)/4$		2.50	6.36	
Total Qty Work Done						402.08	cum
Upto 125%						319.95	cum
Above 125%						82.13	cum


For S.K.S. INFRASTRUCTURES PVT. LTD.,


Contractor Representative
Managing Director



Consultants Representative


Assistant Engineer
Project -RR Nagar Division
BBMP

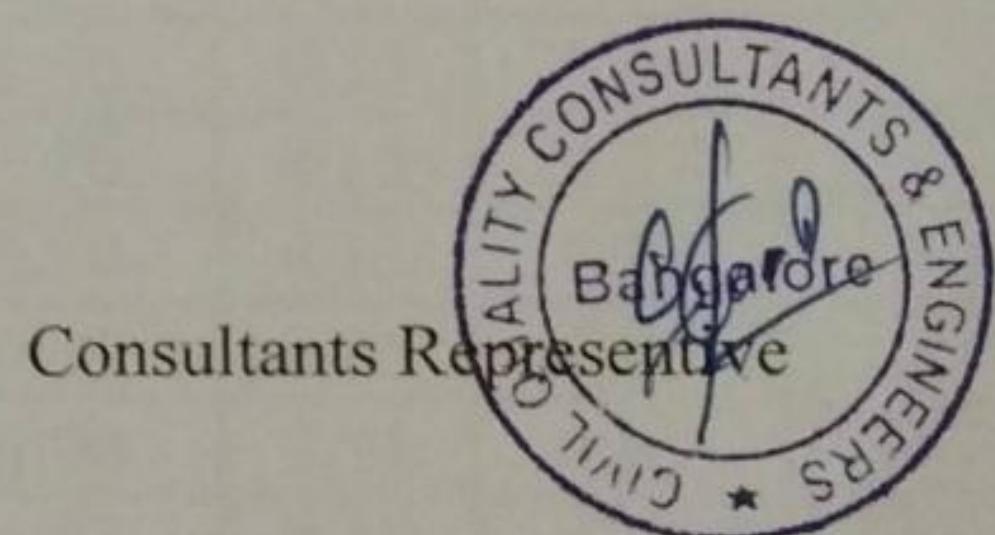

Asst. Executive Engineer
Project -RR Nagar Division
BBMP

BRUHAT BANGALORE MAHANAGARA PALIKE							
NAME OF THE WORK: Modified of Additional works to construction of shuttle cock Ground In Ward No 17 RR Nagar constituency							
Measurement Sheet							
First and Final							
Item No:	3						
Item Name:	Providing and injecting chemical emulsion for Pre-constructional Anti-Termite Treatment, creating continuous chemical barrier under and around the column pits, walls, trenches, basement excavation, top surface of the plinth filling, junction of wall and floor, along the external perimeter of building, expansion joints, over the top surface of consolidated earth on which apron is to be laid, surrounding of pipes and conduits with chloropyriphos emulsifiable concentrates of 20% concentration, including cost of chemical, diluting in water to one percent concentration, labour, HOM of equipments, complete as per specifications. (Plinth area of the building at ground floor only shall be						
	CHAINAGE	NO	L	B	D	QTY	REMARKS
	Land Mark		(m)	(m)	(m)		
	Plinth Area	1	12.95	5.75	--	74.46	
Total Qty Work Done						74.46	sqm
Qty payable in this Bill						74.46	sqm

For S.K.S. INFRASTRUCTURES PVT. LTD.

[Signature]
Contractor Representative
Managing Director

[Signature]
Assistant Engineer
Project -RR Nagar Division
BBMP



Consultants Representative

[Signature]
Asst. Executive Engineer
Project -RR Nagar Division
BBMP

BRUHAT BANGALORE MAHANAGARA PALIKE

**NAME OF THE WORK: Modified of Additional works to construction of shuttle cock
Ground In Ward No 17 RR Nagar constituency**

Measurement Sheet

First and Final

Item No:

4


Item
Name:

Providing and laying in position plain cement concrete of mix 1:3:6 with OPC cement @ 220kgs, with 40mm and down size graded granite metal coarse aggregates @0.892cum and fine aggregates @0.465cum machine mixed, machine mixed, concrete laid in layers not exceeding 15cms, thick, well compacted, in foundation, including cost of all materials, labour, HOM of machinery, curing complete as per specifications. As Per Direction of Engineer Incharge.

		NO	L (m)	B (m)	D (m)	QTY	REMARKS
	Land Mark						
	For RCC Wall	1	51.00	0.60	0.15	4.59	
		1	61.30	0.60	0.15	5.52	
	Building All Round CC Kerb	1	87.00	0.30	0.15	3.92	
		2	24.00	0.30	0.15	2.16	
	For Steps	1	3.50	2.50	0.15	1.31	
		1	2.50	1.50	0.15	0.56	
		1	3.00	1.50	0.15	0.68	
	Fondation bed (Ladies Toilet)	2	12.95	1.10	0.15	4.27	
	Partition wall	1	5.75	0.90	0.15	0.78	
		1	4.63	0.90	0.15	0.63	
		5	2.20	0.90	0.15	1.49	
	Flooring Bed	1	12.50	4.57	0.10	5.71	
	Compound walll	1	13.00	0.90	0.15	1.76	
	Corona	1	5.75	0.90	0.15	0.78	
	Toilet						
	Alround	1	25.00	0.90	0.15	3.38	
	Cross wall	2	6.10	0.90	0.15	1.65	
	do	8	0.80	0.90	0.15	0.86	
	do	1	4.30	0.90	0.15	0.58	
	Flagging	1	21.60	0.75	0.10	1.62	
	Steps	1	1.50	1.50	0.10	0.23	


	Flooring		10	0.90	1.25	0.10	1.13	
	<u>do</u>		1	6.55	1.65	0.10	1.08	
	Alround		1	41.40	0.90	0.15	5.59	
	Cross wall		2	14.55	0.90	0.15	3.93	
	<u>do</u>		2x9	0.80	0.90	0.15	1.94	
	Flagging		1	45.20	0.75	0.10	3.39	
	Steps		1	1.50	1.20	0.10	0.18	
	Flooring		2x4	1.10	1.25	0.10	1.10	
			2x8	1.05	1.25	0.10	2.10	
	<u>do</u>		1	14.85	1.55	0.10	2.30	
			Total Qty Work Done				65.19	CUM
			Qty payable in this Bill				65.19	CUM


For S.K.S. INFRASTRUCTURES PVT. LTD.


Contractor Representative
Managing Director



Consultants Representative


Assistant Engineer
Project -RR Nagar Division
BBMP


Asst. Executive Engineer
Project -RR Nagar Division
BBMP

BRUHAT BANGALORE MAHANAGARA PALIKE

NAME OF THE WORK: Modified of Additional works to construction of shuttle cock
Ground In Ward No 17 RR Nagar constituency

Measurement Sheet

First and Final

Item No:

5


Item
Name:

Providing and constructing granite size stone masonry in foundation with cement mortar 1:6, stone hammered dressed in courses not less than 20cms high, bond stones at 2m. apart in each course including cost of materials, labour, curing complete as per specifications. As Per Direction of Engineer Incharge


CHAINAGE	Land Mark	NO	L	B	D	QTY	REMARKS
			(m)	(m)	(m)		
	For Steps		1	3.50	2.50	0.80	7.00
			1	2.50	1.50	0.80	3.00
			1	3.00	1.50	0.80	3.60
	Ladies Toilet		1	12.95	0.95	0.60	7.38
			1	12.95	0.75	0.60	5.83
	Partition Wall		1	5.75	0.75	0.80	3.45
			1	12.95	0.60	0.60	4.66
			1	5.75	0.60	0.80	2.76
			5	2.20	0.60	0.80	5.28
			5	2.20	0.75	0.80	6.60
	Compound wall		1	13.00	0.60	0.60	4.68
	Lab Compound Wall						
	Basement		1	16.70	0.75	0.45	5.64
			1	16.70	0.45	0.45	3.38
	Toilet Block						
	<u>1st Coarse</u>						
	Alround		1	25.00	0.75	0.40	7.50
	Cross wall		2	6.25	0.75	0.40	3.75
	do		8	0.95	0.75	0.40	2.28
	do		1	4.30	0.75	0.40	1.29
	<u>2nd Coarse</u>						
	Alround		1	25.00	0.60	0.40	6.00


Cross wall		2	6.40	0.60	0.40	3.07	
do		8	1.10	0.60	0.40	2.11	
do		1	4.30	0.60	0.40	1.03	
<u>1st Coarse</u>							
Alround		1	41.40	0.75	0.45	13.97	
Cross wall		2	14.70	0.75	0.45	9.92	
do		2x9	0.95	0.75	0.45	5.77	
<u>2nd Coarse</u>							
Alround		1	41.40	0.60	0.45	11.18	
Cross wall		2	14.85	0.60	0.45	8.02	
do		2x9	1.10	0.60	0.45	5.35	
			Total Qty Work Done			144.50	cum
Qty payable in this Upto 125%						89.74	cum
Qty payable in this Above 125%						54.77	cum

For S.K.S. INFRASTRUCTURES PVT. LTD.


Contractor Representative
Managing Director



Consultants Representative



Assistant Engineer
Project -RR Nagar Division
BBMP


Asst. Executive Engineer
Project -RR Nagar Division
BBMP

BRUHAT BANGALORE MAHANAGARA PALIKE							
NAME OF THE WORK: Modified of Additional works to construction of shuttle cock Ground In Ward No 17 RR Nagar constituency							
Measurement Sheet							
First and Final							
Item No:	6						
Item Name:	Providing and Constructing Granite /size stone masonry in Basement with cement mortor 1:6, stone hammered dressed in courses not less than 20cms high, bond stones at 2m. apart in each course including cost of materaials, labour, curing complete asper specifications. As Per Direction of Engineer Incharge						
	CHAINAGE	NO	L	B	D	QTY	REMARKS
	Land Mark		(m)	(m)	(m)		
	Ladies Toilet	1	12.95	0.45	0.40	2.33	
	partition Wall	1	5.75	0.45	0.40	1.04	
	Compound Wall	1	13.00	0.45	0.40	2.34	
	toliet block						
	Alround	1	25.00	0.45	0.45	5.06	
	Cross wall	2	6.55	0.45	0.45	2.65	
	do	8	1.25	0.45	0.45	2.03	
	do	1	4.30	0.45	0.45	0.87	
	Alround	1	41.40	0.45	0.45	8.38	
	Cross wall	2	14.85	0.45	0.45	6.01	
	do	2x9	1.25	0.45	0.45	4.56	
			Total Qty Work Done			35.27	cum
Qty payable in this Upto 125%						7.14	cum
Qty payable in this Above 125%						28.13	cum


For S.K.S. INFRASTRUCTURES PVT. LTD.


Contractor Representative
Managing Director


Assistant Engineer
Project -RR Nagar Division
BBMP



Consultants Representative


Asst. Executive Engineer
Project -RR Nagar Division
BBMP

BRUHAT BANGALORE MAHANAGARA PALIKE

NAME OF THE WORK: Modified of Additional works to construction of shuttle
sock Ground In Ward No 17 RR Nagar constituency

Measurement Sheet

First and Final

Item No:

7

Item
Name:

Providing and laying in position plain cement concrete of mix 1:2:4 with cement @ 240kgs, with 20mm and down size graded granite metal coarse aggregates @ 0.69 cum and fine aggregates @ 0.459cum, machine mixed, concrete laid in layers not exceeding 15 cms. thick, well compacted, in foundation, plinth and cills, including cost of all materials, labour, HOM of machinery, curing complete as per specifications. As Per Direction of Engineer Incharge

CHAINAGE Land Mark	NO	L (m)	B (m)	D (m)	QTY	REMARKS
Coping						
	1	12.95	0.45	0.15	0.87	
	1	5.75	0.45	0.15	0.39	
Compound Wall	1	13.00	0.45	0.15	0.88	
Toilet block						
Flagging	1	21.60	0.75	0.10	1.62	
Plinth						
Around	1	25.00	0.45	0.15	1.69	
Cross wall	2	6.55	0.45	0.15	0.88	
do	8	1.25	0.45	0.15	0.68	
do	1	4.30	0.45	0.15	0.29	
Flagging	1	45.20	0.75	0.10	3.39	
Plinth						
Around	1	41.40	0.45	0.15	2.79	
Cross wall	2	14.85	0.45	0.15	2.00	

	do		2x9	1.25	0.45	0.15	1.52	
				Total Qty Work Done			17.00	cum
Qty payable in this Upto 125%							2.68	cum
Qty payable in this Above 125%							14.33	cum

For S.K.S. INFRASTRUCTURES PVT. LTD.

B. S.
Contractor Representative
Managing Director



B. K. Dhanu
Assistant Engineer
Project -RR Nagar Division
BBMP

B. K. Dhanu
Asst. Executive Engineer
Project -RR Nagar Division
BBMP

BRUHAT BANGALORE MAHANAGARA PALIKE								
NAME OF THE WORK: Modified of Additional works to construction of shuttle cock Ground In Ward No 17 RR Nagar constituency								
Measurement Sheet								
First and Final								
Item No:	8							
Item Name:	Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for foundations, footings, bases of columns for mass concrete including cost of all materials, labour complete as per specifications. As Per Direction of Engineer Incharge							
	CHAINAGE		NO	L	B	D	QTY	REMARKS
	Land Mark			(m)	(m)	(m)		
	For RCC Wall Footing		2	51.00	--	0.30	30.60	
			2	61.30	--	0.30	36.78	
			Total Qty Work Done				67.38	Sqm
			Qty payable in this Bill				67.38	Sqm


For S.K.S. INFRASTRUCTURES PVT. LTD.


Contractor Representative


Managing Director



Consultant Representative




Assistant Engineer
Project -RR Nagar Division
BBMP




Asst. Executive Engineer
Project -RR Nagar Division
BBMP

BRUHAT BANGALORE MAHANAGARA PALIKE							
NAME OF THE WORK: Modified of Additional works to construction of shuttle cock Ground In Ward No 17 RR Nagar constituency							
Measurement Sheet							
First and Final							
Item No:	9						
Item Name:	Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for vertical surface such as walls at any thickness, attached pilasters, bittresses, plinth and string course including cost of all materials, labour complete as per specifications. Specification NO KBS 4.6.2As Per Direction of Engineer Incharge						
	CHAINAGE	NO	L	B	D	QTY	REMARKS
	Land Mark		(m)	(m)	(m)		
	For RCC Wall	2	51.00	--	1.00	102.00	
		2	61.30	--	1.00	122.60	
	Water Storage Tank Room	1	9.14	--	0.15	1.37	
	Compound Wall						
	Plinth Beam	2	16.70		0.20	6.68	
	Toilet block						
	<u>Plinth</u>						
	~~Around~~	1x2	25.00	-	0.15	7.50	
	Cross wall	2x2	6.55	-	0.15	3.93	
	<u>do</u>	8x2	1.25	-	0.15	3.00	
	<u>do</u>	1x2	4.30	-	0.15	1.29	
	<u>Plinth</u>						
	~~Around~~	1x2	41.40	-	0.15	12.42	
	Cross wall	2x2	14.85	-	0.15	8.91	
	<u>do</u>	4x9	1.25	-	0.15	6.75	
			Total Qty Work Done			276.45	sqm
			Qty payable in this Bill			276.45	sqm


For S.K.S. INFRASTRUCTURES PVT. LTD.,


Contractor Representative
Managing Director


Assistant Engineer
Project -RR Nagar Division
BBMP



Consultants Representative


Asst. Executive Engineer
Project -RR Nagar Division
BBMP

BRUHAT BANGALORE MAHANAGARA PALIKE


NAME OF THE WORK: Modified of Additional works to construction of shuttle cock
Ground In Ward No 17 RR Nagar constituency


Measurement Sheet


First and Final


Item No:	10						
Item Name:	Providing and removing centering, shuttering, strutting, propping etc., an removal of form work for sides & soffits of beams, beam hauncing cantilever girders, bressumers & lintels & not exceeding 1.0 in depth including cost of all materials, labour complete as per specifications. - As Per Direction of Engineer Incharge						
	CHAINAGE	NO	L	B	D	QTY	REMARKS
	Land Mark		(m)	(m)	(m)		
	For RCC Plinth Beam	4	12.95	--	0.30	15.54	
		8	2.15	--	0.30	5.16	
		8	4.70	--	0.30	11.28	
		4	1.06	--	0.30	1.27	
		2	5.75	--	0.30	3.45	
	For RCC Chejja	3	1.00	--	0.60	1.80	
		3	2.20	--	0.10	0.66	
		1	1.60	--	0.60	0.96	
	For RCC Lintel	3	0.90	--	0.15	0.41	
		1	1.50	--	0.15	0.23	
		1	2.00	--	0.10	0.20	
		2	12.95	--	0.20	5.18	
		4	4.63	--	0.20	3.70	
		1	0.90	--	0.20	0.18	
		2	1.20	--	0.20	0.48	
	For Roof Beam	2	12.95	--	0.45	11.66	
		2	4.63	--	0.45	4.16	
		6	4.63	--	0.30	8.33	
		2	12.50	--	0.30	7.50	
		1	12.50	--	0.15	1.88	
	Toilet block						
	<u>Lintel</u>						
	~~Around~~	1x2	25.00	-	0.15	7.50	
	Cross wall	1x2	6.80	-	0.15	2.04	
	<u>do</u>	1x2	5.40	-	0.15	1.62	
	<u>do</u>	1x2	4.30	-	0.15	1.29	
	<u>Lintel</u>						

	Alround		1x2	41.40	-	0.15	12.42	
	Cross wall		2x2	15.10	-	0.15	9.06	
				Total Qty Work Done			117.94	sqm
Qty payable in this Upto 125%							105.01	sqm
Qty payable in this Above 125%							12.93	sqm

For S.K.S. INFRASTRUCTURES PVT. LTD.

Contractor Representative
Managing Director

CONSULTANTS & ENGINEERS
BANGALORE

Consultants Representative


Assistant Engineer
Project -RR Nagar Division
BBMP


Asst. Executive Engineer
Project -RR Nagar Division
BBMP

BRUHAT BANGALORE MAHANAGARA PALIKE

**NAME OF THE WORK: Modified of Additional works to construction of shuttle cock
Ground In Ward No 17 RR Nagar constituency**

Measurement Sheet

First and Final

Item No:


11

Item
Name:

Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for Flat surfces such as suspended floors ,roofs,landings,balconies and likes,thickness above 200mm including cost of all materials, labour complete as per specifications. As Per Direction of Engineer Incharge


CHAINAGE Land Mark	NO	L (m)	B (m)	D (m)	QTY	REMARKS
For RCC Roof	1	12.80	--	4.55	58.24	
Water Storage tank	1	2.50	--	2.14	5.35	
		Total Qty Work Done			63.59	sqm
		Qty payable in this Bill			63.59	sqm


For S.K.S. INFRASTRUCTURES PVT. LTD


Contractor Representative
Managing Director



Consultants Representative



Assistant Engineer
Project -RR Nagar Division
BBMP


Asst.Executive Engineer
Project -RR Nagar Division
BBMP


BRUHAT BANGALORE MAHANAGARA PALIKE							
NAME OF THE WORK: Modified of Additional works to construction of shuttle cock Ground In Ward No 17 RR Nagar constituency							
Measurement Sheet							
First and Final							
Item No:	12						
Item Name:	Providing and laying in position plain reinforced cement concrete of design mix M25 with OPC cement @ 340kgs, with 20mm and down size graded granite metal coarse aggregates @0.70cum and fine aggregates @0.47cum, with superplasticisers @3ltrs confirming to IS9103-1999 Reaffirmed -2008, machine mixed, concrete laid in layers not exceeding 15cms thick, vibrated for all works in ground floor level for roof slabs, staircase, lintels and beams retaining walls, return walls, walls(any thickness) including attached plasters, columns, pillars, posts, struts, buttresses, string or lacing courses, parapets, coping, bed blocks, anchor blocks, plain window cills, fillets etc, including cost of all materials, labour HOM of machinery, curing, complete as per specifications. Specification. As Per Direction of Engineer Incharge						
	CHAINAGE	NO	L	B	D	QTY	REMARKS
	Land Mark		(m)	(m)	(m)		
	For RCC Wall Footing	1	51.00	0.60	0.30	9.18	
		1	61.30	0.60	0.30	11.03	
	For RCC Wall	1	51.00	0.15	1.00	7.65	
		1	61.30	0.15	1.00	9.20	
	For RCC Plinth Beam	2	12.95	0.30	0.30	2.33	
	For RCC Roof Beam	2	13.10	0.15	0.30	1.18	
		3	4.40	0.15	0.30	0.59	
		1	4.63	0.30	0.30	0.42	
	RCC Lintel	1	12.95	0.15	0.30	0.58	
		1	4.63	0.15	0.30	0.21	
	RCC Roof Slab	1	13.10	4.70	0.15	9.24	
	Water Storage Tank Room	1	2.50	2.50	0.15	0.94	
	Compound						
	Plinth Beam	1	16.70	0.45	0.20	1.50	
	Toilet block						
	Lintel Concrete						
	Alround	1	25.00	0.20	0.15	0.75	
	Cross wall	1	6.80	0.20	0.15	0.20	
	do	1	5.40	0.20	0.15	0.16	
	do	1	4.30	0.20	0.15	0.13	
	Lintel Concrete						
	Alround	1	41.40	0.20	0.15	1.24	


	Cross wall		2	15.10	0.20	0.15	0.91	
			Total Qty Work Done				57.44	Sqm
			Qty payable in this Bill				57.44	Sqm

For S.K.S. INFRASTRUCTURES PVT. LTD.,


Contractor Representative
Managing Director




Assistant Engineer
Project -RR Nagar Division
BBMP


Asst. Executive Engineer
Project -RR Nagar Division
BBMP

BRUHAT BANGALORE MAHANAGARA PALIKE							
NAME OF THE WORK: Modified of Additional works to construction of shuttle cock Ground In Ward No 17 RR Nagar constituency							
Measurement Sheet							
First and Final							
Item No:	13						
Item Name:	Providing and laying i position Reinforced cement concrete of design Mix M20 with OPC @ 27.20kgs, with 12mm and Down Size graded granite metal coarse aggregate @ 0.05865cum and fine aggregate @0.0391 cum, with Super plasticisers @0.225lts, machine mixed , well compacted for plain Chajja of 8.5cms. Average thickness ,upto ground floor level, including cost of all materials, labour HOM of machinery, curing, complete as per specifications. Specification. As Per Direction of Engineer Incharge						
	CHAINAGE	NO	L	B	D	QTY	REMARKS
	Land Mark		(m)	(m)	(m)		
	RCC Chajja	1	5.00	--	0.60	3.00	
		2	2.00	--	0.60	2.40	
	Toilet block						
	Chajja Concrete						
	D	1	1.20	-	0.60	0.72	
	V	13	0.90	-	0.60	7.02	
	Chajja Concrete						
	D	1	1.20	-	0.60	0.72	
	V	20	0.90	-	0.60	10.80	
			Total Qty Work Done			24.66	cum
Qty payable in this Upto 125%						6.75	cum
Qty payable in this Above 125%						17.91	cum

For S.K.S. INFRASTRUCTURES PVT. LTD.

Contractor Representative

Managing Director

R. K. G. R. R.

Assistant Engineer
Project -RR Nagar Division
BBMP



Consultants Representative


R. K. G. R. R.


Asst. Executive Engineer
Project -RR Nagar Division
BBMP

BRUHAT BANGALORE MAHANAGARA PALIKE										
NAME OF THE WORK: Modified of Additional works to construction of shuttle cock Ground In Ward No 17 RR Nagar constituency										
Measurement Sheet										
First and Final										
Item No:	14									
Item Name:	KSRB: 4.9.2: Providing TMT Bars of Fe 500 steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, placing in position, lapping and / or welding wherever required, fixing with binding wire and anchoring to the adjoining members wherever necessary complete as per design, (laps and wastages shall not be measured and paid) csot of materials, etc. complete as per specifications									
SLNO	CHAINAGE		NO	L	B	BI	Avg B	D	QTY	REMARKS
	Land Mark			(m)	(m)	(m)	(m)	(m)		
	Footing									
	10		mm dia							
			2	5	51.00	=	489.60			
			2	5	61.30	=	588.48			
							1078.08	mtr		
						@	0.62	665.48	Kgs	
	12		mm dia							
			2	408	0.60	=	489.60			
			2	490	0.60	=	588.48			
							1078.08	mtr		
						@	0.89	958.29	Kgs	
	Wall									
	12		mm dia							
			2	8	51.00	=	816.00			
			2	8	61.30	=	980.80			
							1796.80	mtr		
						@	0.89	1597.16	Kgs	
	12		mm dia							
			2	408	1.25	=	1020.00			
			2	490	1.25	=	1226.00			
							2246.00	mtr		
						@	0.89	1996.44	Kgs	
	Plinth Beam & RB									
	16		mm dia							
			2	6	12.95	=	155.40			
			2	4	13.10	=	104.80			
			3	4	4.40	=	52.80			
			1	4	4.63	=	18.52			
							331.52	mtr		
						@	1.58	523.88	Kgs	
	8		mm dia							
			2	104	0.90	=	186.48			
			2	105	0.60	=	125.76			
			3	35	0.60	=	63.36			
			1	37	0.60	=	22.22			
							397.82	mtr		
						@	0.40	157.17	Kgs	

Lintel									
12		mm dia							
		1	4	147.00	=	588.00			
						588.00	mtr		
					@	0.89	522.67	Kgs	
8		mm dia							
		1	1470	0.90	=	1323.00			
						1323.00	mtr		
					@	0.40	522.67	Kgs	
Roof Slab									
12		mm dia							
		1	50	13.45	=	665.78			
		1	135	4.95	=	665.78			
Extra Bar		5	40	2.50	=	495.00			
		4	105	2.50	=	1050.00			
						2876.55	mtr		
					@	0.89	2556.93	Kgs	
Storage Tank									
12		mm dia							
		1	28	2.75	=	75.63			
		1	28	2.75	=	75.63			
Extra Bar		3	28	2.20	=	181.50			
		3	28	2.20	=	181.50			
						514.25	mtr		
					@	0.89	457.11	Kgs	
Chejja									
10		mm dia							
V		33	6	0.90	=	178.20			
		33	9	0.60	=	178.20			
V		1	6	5.00	=	30.00			
		1	50	0.60	=	30.00			
V		2	6	2.00	=	24.00			
		2	20	0.60	=	24.00			
D		2	6	1.20	=	14.40			
		2	12	0.60	=	14.40			
						493.20	mtr		
					@	0.62	304.44	Kgs	
Total Qty						10262.25	Kg/mtr		
Total Qty Work Done						10.26	Tonne		
Qty Payable in this bill						10.19	Tonne		


For S.K.S. INFRASTRUCTURES PVT. LTD.


Contractor Representative
Managing Director


Assistant Engineer
Ward No 16




Consultant Representative



Asst. Executive Engineer
Yashwanthapura Sub Division


BRUHAT BANGALORE MAHANAGARA PALIKE							
NAME OF THE WORK: Modified of Additional works to construction of shuttle cock Ground In Ward No 17 RR Nagar constituency							
Measurement Sheet							
First and Final							
Item No:	15						
Item Name:	Providing and applying ready mix priming coat over concrete/masonry/asbestos cement sheet/plastered surfaces including preparing the surface after thoroughly cleaning of oil, grease,dirt and other foreign matter, and papering including cost of materials, labour ,complete as per specifications.As Per Direction of Engineer Incharge						
	CHAINAGE Land Mark	NO	L (m)	B (m)	D (m)	QTY	REMARKS
	Building All Round CC Kerb	1	87.00	0.30	--	26.10	
		2	24.00	0.30	--	14.40	
		1	10.00	0.30	--	3.00	
	For RCC Wall (Kerb)	2	51.00	--	1.00	102.00	
		2	61.30	--	1.00	122.60	
			Total Qty Work Done			268.10	Sqm
			Qty payable in this Bill			268.10	Sqm

For S.K.S. INFRASTRUCTURES PVT. LTD.


Contractor Representative
Project Director


Consultants Representative
Bangalore


Assistant Engineer
Project -RR Nagar Division
BBMP


Asst. Executive Engineer
Project -RR Nagar Division
BBMP

BRUHAT BANGALORE MAHANAGARA PALIKE							
NAME OF THE WORK: Modified of Additional works to construction of shuttle cock Ground In Ward No 17 RR Nagar constituency							
Measurement Sheet							
First and Final							
Item No:	16						
Item Name:	Provoding and applying ready mix spray painting in two coat over concrete/masonry/asbestos cement sheet/platered surfaces including preparing the surface after thoroughly cleaning of oil, grease,dirt and other foreign matter, and papering including cost of materials, labour ,complete as per specifications.As Per						
	CHAINAGE	NO	L	B	D	QTY	REMARKS
	Land Mark		(m)	(m)	(m)		
	Building All Round CC Kerb	1	87.00	0.30	--	26.10 ✓	
		2	24.00	0.30	--	14.40	
		1	10.00	0.30	--	3.00 ✓	
	For RCC Wall (Kerb)	2	51.00	--	0.60	61.20 ✓	
		2	61.30	--	0.60	73.56 ✓	
			Total Qty Work Done			178.26	Sqm
			Qty payable in this Bill			178.26	Sqm

For S.K.S. INFRASTRUCTURES PVT. LTD.

Contractor Representative

Managing Director

S.K. Durbeykar

Assistant Engineer
Project -RR Nagar Division
BBMP



Consultant's Representative


S.K. Durbeykar

Asst.Executive Engineer
Project -RR Nagar Division
BBMP

BRUHAT BANGALORE MAHANAGARA PALIKE							
NAME OF THE WORK: Modified of Additional works to construction of shuttle cock Ground In Ward No 17 RR Nagar constituency							
Measurement Sheet							
First and Final							
Item No:	17						
Item Name:	Providing and constructing Precast concrete solid blocks with compressive strenght not less than 35Kg/sqm with cement mortar 1:4 masonry (quion, Jamb, closer blocks) with solid concrete blocks of size 40x15x20cms confirming to IS:2185/1965 in superstructure including cost of materials, labour charges, scalffolding, curing etc., complete as per specifications. As Per Direction of Engineer Incharge						
	CHAINAGE	NO	L	B	D	QTY	REMARKS
	Land Mark		(m)	(m)	(m)		
	Front Steps						
		1	3.30	0.15	--	0.50 ✓	
		1	2.90	0.15	--	0.44	
		1	2.50	0.15	--	0.38	
		1	2.10	0.15	--	0.32	
		1	1.70	0.15	--	0.26	
		5	3.30	0.40	--	6.60	
	Stadium Ent Step						
	Field To Road	1	2.40	3.30	--	7.92 ✓	
		1	2.00	3.30	--	6.60	
		1	1.60	3.30	--	5.28	
		1	1.20	3.30	--	3.96	
		1	0.80	3.30	--	2.64	
		1	0.40	3.30	--	1.32	
	Building Ent						
		1	0.90	--	3.00	2.70 ✓	
		1	0.60	--	3.00	1.80	
		1	0.30	--	3.00	0.90 ✓	
	Building Ent 2			--			
		1	0.90	--	2.30	2.07	
		1	0.60	--	2.30	1.38	
		1	0.30	--	2.30	0.69	
	Ladies Toilet Wall			--			
		2	12.95	--	3.60	93.24 ✓	
		2	4.63	--	3.60	33.30 ✓	
		1	4.57	--	3.00	13.71	
	Parapet Wall	2	12.95	--	1.00	25.90	
		2	4.57	--	1.00	9.14 ✓	
	Water Storage Tank Room	2	2.50	--	2.14	10.70	


		1	2.10	--	2.14	4.49 ✓	
		1	10.00	--	0.80	8.00	
		1	6.22	--	3.00	18.66	
						262.88 ✓	
	Deductions						
	V	-4	0.75	--	0.75	-2.25	
	V1	-2	2.10	--	1.20	-5.04	
	Door	-2	0.75	--	2.10	-3.15	
		-1	1.20	--	2.10	-2.52	
		-1	1.20	--	2.20	-2.64	
		-2	1.10	--	0.60	-1.32	
		-1	1.25	--	2.10	-2.63	
		-2	0.75	--	2.10	-3.15	
						-22.70	
						240.18	
	labs						
	New Wall						
		1	4.75		2.60	12.35	
		Total Qty Work Done				252.53	Sqm
		Qty payable in this Bill				252.53	Sqm


For S.K.S. INFRASTRUCTURES PVT. LTD.


Contractor Representative
Managing Director



Consultants Representative



Assistant Engineer
Project -RR Nagar Division
BBMP


Asst. Executive Engineer
Project -RR Nagar Division
BBMP

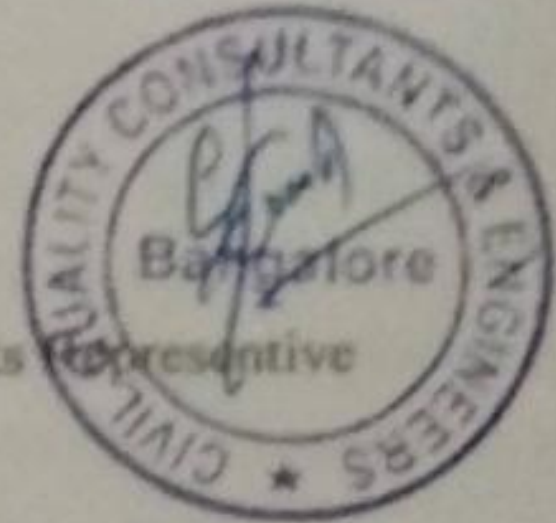
BRUHAT BANGALORE MAHANAGARA PALIKE							
NAME OF THE WORK: Modified of Additional works to construction of shuttle cock Ground In Ward No 17 RR Nagar constituency							
Measurement Sheet							
First and Final							
Item No:	18						
Item Name:	Providing and constructing non-load bearing wall with Solid cement concrete solid blocks of size 400x100x200mm having a block density not less than 1800 Kg/m3 having a minimum average compressive strength of 4.00 N/mm2 confirming to I.S: 2185 (part 1):2005 and constructed with CM 1:4, as per IS 2572:2005 including cost of materials, labour charges, scaffolding, curing, hire charges of machineries etc., complete as per specifications. KBS No. 5.4 As Per Direction of Engineer Incharge						
	CHAINAGE	NO	L	B	D	QTY	REMARKS
	Land Mark		(m)	(m)	(m)		
	Toilet Partiti	Cum	4	2	1	3	24.00
			1	4.4	1	3	13.20
			1	1.1	1	3	3.30
							40.50
	Deductions						
	Door		-1	4	0.75	2.1	-6.30
							34.20
	Toilet block						
	Cross wall		8	1.50	-	2.40	28.80
	do		1	4.30	-	2.40	10.32
	Front steps		1	1.50	-	1.50	2.25
	do		1	1.50	-	1.20	1.80
	do		1	1.50	-	0.90	1.35
	do		1	1.50	-	0.60	0.90
	do		1	1.50	-	0.30	0.45
	Cross wall		9x2	1.50	-	2.40	64.80
	Front steps		1	1.50	-	1.50	2.25
	do		1	1.50	-	1.20	1.80
	do		1	1.50	-	0.90	1.35
	do		1	1.50	-	0.60	0.90

	do		1	1.50	-	0.30	0.45	
				Total Qty Work Done			151.62	Sqm
				Qty payable in this Upto 125%			56.34	Sqm
				Qty payable in this Above 125%			95.28	Sqm


For S.K.S. INFRASTRUCTURES PVT. LTD.




Contractor Representative
Managing Director



Consultants Representative




Assistant Engineer
Project -RR Nagar Division
BBMP




Asst. Executive Engineer
Project -RR Nagar Division
BBMP

BRUHAT BANGALORE MAHANAGARA PALIKE							
NAME OF THE WORK: Modified of Additional works to construction of shuttle cock Ground In Ward No 17 RR Nagar constituency							
Measurement Sheet							
First and Final							
Item No:	19						
Item Name:	providing and fixing Vitrifiedglazed tiles of approved make, quality & Colour of size 1000 x 1000 x 12mm/ 800mm x 1200mm x 12mm thick fixed on bed of 12mm thick cement mortor for flooring, skirting and jointed with neat cement slurry mixed with pigment to mach shade of tiles, including providing spacers at required interval and removing stains , including cost of all materials , mortor, labour,etc., complete as per specifications. (Market Rate)						
	CHAINAGE	NO	L	B	D	QTY	REMARKS
	Land Mark		(m)	(m)	(m)		
	Waiting Room	3	4.60	6.30	--	86.94	
	Mazzine Flooring top	1	20.80	5.70	--	118.56	
	Office Room	1	7.50	4.60	--	34.50	
	Toilet Enterance and Was	1	2.12	2.50	--	5.30	
		1	4.45	2.32	--	10.32	
	Skirting	1	2.35	2.25	--	5.29	
	Waiting Room	1	21.80	--	0.10	2.18	
	Office Room	1	23.10	--	0.10	2.31	
	Toilet Enterance and Was	1	9.24	--	0.10	0.92	
			Total Qty Work Done			266.33	Sqm
			Qty payable in this Bill			266.33	Sqm

For S.K.S. INFRASTRUCTURES PVT. LTD.



Contractor Representative

Managing Director


Assistant Engineer
Project -RR Nagar Division
BBMP




Consultants Representative


Asst. Executive Engineer
Project -RR Nagar Division
BBMP

BRUHAT BANGALORE MAHANAGARA PALIKE								
NAME OF THE WORK: Modified of Additional works to construction of shuttle cock Ground In Ward No 17 RR Nagar constituency								
Measurement Sheet								
First and Final								
Item No:	20							
Item Name:	Supply and installation of approved wooden floor for Indoor Hall-Maple Flooring with PU Sealer and coat polish 20mm, Thickness X 60mm Width X 200mm, third & better grade treated Sleeper of size 30X60mm to be installed 30cm centre to centre 20m professional EPDM Rubber pad inclusive of HOM, Labour etc. as per the direction of the Engineer in Charge (Data Approved							
	CHAINAGE		NO	L	B	D	QTY	REMARKS
	Land Mark			(m)	(m)	(m)		
	HALL		1	20.80	45.55	--	947.44	} added
	Deduct Coloumns		-24	0.20	0.70	--	-3.36	
			Total Qty Work Done				944.08	Sqm
			Qty payable in this Bill				944.08	Sqm


For S.K.S. INFRASTRUCTURES PVT. LTD.



Contractor Representative

Managing Director




Consultant's Representative


Assistant Engineer
Project -RR Nagar Division
BBMP


Asst. Executive Engineer
Project -RR Nagar Division
BBMP


BRUHAT BANGALORE MAHANAGARA PALIKE								
NAME OF THE WORK: Modified of Additional works to construction of shuttle cock Ground In Ward No 17 RR Nagar constituency								
Measurement Sheet								
First and Final								
Item No:	21							
Item Name:	Providing and fixing BWF Standards lime marking and painting using LUSTRE Paint for 13.41 x 6m with 400mm Wide limes settle cock flight checking markings including Labour and transplotation (Data Aproved Rate)As Per Direction of Engineer Incharge							
	CHAINAGE		NO	L	B	D	QTY	REMARKS
	Land Mark			(m)	(m)	(m)		
			6	-	-	-	6.00	
			Total Qty Work Done				6.00	Sqm
			Qty payable in this Bill				6.00	Sqm


For S.K.S. INFRASTRUCTURES PVT. LTD;


Contractor Representative
Managing Director




Consultants Representative



Assistant Engineer
Project -RR Nagar Division
BBMP


Asst. Executive Engineer
Project -RR Nagar Division
BBMP


BRUHAT BANGALORE MAHANAGARA PALIKE							
NAME OF THE WORK: Modified of Additional works to construction of shuttle cock Ground In Ward No 17 RR Nagar constituency							
Measurement Sheet							
First and Final							
Item No:	22						
Item Name:	Supplying and fixing net pole total weight 200Kg material used Corborundum poles gauge 14 gear top wheel type metal paint type Epoxy paintng movable type portable on wheels Height 5.1ft tapered box with yonex Standard net as per Specifications etc, Complete including transporting Instalation at Site (Data aproved Rate)As Per						
CHAINAGE		NO	L	B	D	QTY	REMARKS
Land Mark			(m)	(m)	(m)		
		6	-	-	-	6.00	
		Total Qty Work Done				6.00	EACH
		Qty payable in this Bill				6.00	EACH

For S.K.S. INFRASTRUCTURES PVT. LTD.


Contractor Representative
Managing Director


Assistant Engineer
Project -RR Nagar Division
BBMP





Asst. Executive Engineer
Project -RR Nagar Division
BBMP

BRUHAT BANGALORE MAHANAGARA PALIKE							
NAME OF THE WORK: Modified of Additional works to construction of shuttle cock Ground In Ward No 17 RR Nagar constituency							
Measurement Sheet							
First and Final							
Item No:	23						
Item Name:	Providing and laying pattern flooring for staircase treads and risers using the combination 20mm thick ruby red granite @ 66%, 20 mm thick grey granite @ 20%, 20mm thick 20mm thick black granite 14%. The granite materials are laid on existing bed of CM 1:3 20mm thick pointed with colour pigment, including full rounding for nosing, flaming the ruby red granite for 50mm wide curing etc., wide curing etc., complete. As Per Direction of Engineer Incharge						
	CHAINAGE	NO	L	B	D	QTY	REMARKS
	Land Mark		(m)	(m)	(m)		
	Toilet Ent Door Granite	1	6.40	0.30	--	1.92	
		1	5.30	0.30	--	1.59	
		1	5.30	0.30	--	1.59	
		1	4.80	0.30	--	1.44	
	Ventilator and Windows	5	3.00	0.30	--	4.50	
		1	6.80	0.30		2.04	
	Office Doors	1	5.35	0.30	--	1.61	
	Waiting Room	1	9.46	0.30	--	2.84	
	Wooden Box Top	22	4.40	0.55	--	53.24	
		5	3.60	0.55	--	9.90	
	Front Steps						
		1	3.30	1.20	--	3.96	
		1	3.30	0.15	--	0.50	
		6	3.30	0.40	--	7.92	
		6	3.30	0.15	--	2.97	
	Stadium Ent Step						
		4	3.00	0.30	--	3.60	
		4	3.00	0.15	--	1.80	
		4	2.30	0.30	--	2.76	


			4	2.30	0.15	--	1.38	
			Total Qty Work Done				105.55	SQM
			Qty payable in this Bill				105.55	SQM


For S.K.S. INFRASTRUCTURES PVT. LTD.


Contractor Representative
Managing Director



Consultants Representative


Assistant Engineer
Project -RR Nagar Division
BBMP


Asst. Executive Engineer
Project -RR Nagar Division
BBMP

BRUHAT BANGALORE MAHANAGARA PALIKE							
NAME OF THE WORK: Modified of Additional works to construction of shuttle cock Ground In Ward No 17 RR Nagar constituency							
Measurement Sheet							
First and Final							
Item No:	24						
Item Name:	For Ceiling Plastering:- Providing 12mm thick cement plaster in single coat with cement mortar 1:4, to ceiling including rounding off corners wherever required smooth rendering, : Providing and removing scaffolding, including cost of materials, labour, curing complete as per specifications. As Per Direction of Engineer Incharge						
	CHAINAGE	NO	L	B	D	QTY	REMARKS
	Land Mark		(m)	(m)	(m)		
	Toilets	1	12.65	4.57		57.81 ✓	
	Water Storage tank room	1	2.43	2.43		5.90 ✓	
	Toilet block						
	Ceiling	1	12.80	5.60	-	71.68 ✓	
			Total Qty Work Done			135.40 ✓	
			Qty payable in this Upto 125%			79.65	sqm
			Qty payable in this Above 125%			55.75	sqm

For S.K.S. INFRASTRUCTURES PVT. LTD.

[Signature]
Contractor Representative
Managing Director

CIVIL QUALITY CONSULTANTS & ENGINEERS
Bangalore

[Signature]
Consultants Representative


[Signature]
Assistant Engineer
Project -RR Nagar Division
BBMP


[Signature]
Asst.Executive Engineer
Project -RR Nagar Division
BBMP

BRUHAT BANGALORE MAHANAGARA PALIKE							
NAME OF THE WORK: Modified of Additional works to construction of shuttle cock Ground In Ward No 17 RR Nagar constituency							
Measurement Sheet							
First and Final							
Item No:	25						
Item Name:	Plastering-Internal:- Providing 18mm thick cement plaster in single coat with cement mortar 1:4, to brick masonry including rounding off corners wherever required smooth rendering: Providing and removing scaffolding, Providing Lime rendering for plastering to ceiling including cost of materials, labour, curing complete as per specifications. As Per Direction of Engineer Incharge						
	CHAINAGE	NO	L	B	D	QTY	REMARKS
	Land Mark		(m)	(m)	(m)		
	For dadooing						
	Gents Toilet						
		1	2.50	--	3.00	7.50	
		1	4.50	--	3.00	13.50	
		1	1.15	--	3.00	3.45	
		1	2.40	--	3.00	7.20	
		1	1.30	--	3.00	3.90	
		1	2.00	--	3.00	6.00	
	Toilet						
		2	2.15	--	3.00	12.90	
		2	2.35	--	3.00	14.10	
	Ladies Toilet	2	12.50	--	3.00	75.00	
		6	4.57	--	3.00	82.26	
		8	2.20	--	3.00	52.80	
		2	1.06	--	3.00	6.36	
		1	6.20	--	3.00	18.60	
						303.57	
	Deduction						
	D2	-2	0.75	--	2.05	-3.08	
	V	-2	0.90	--	0.60	-1.08	
		-1	1.50		0.60	-0.90	
	V1	-2	0.90		0.60	-1.08	
	D1	-3	1.20	--	2.05	-7.38	
	D	-1	0.70	--	2.05	-1.44	
		-9	0.75	--	2.10	-14.18	
		-1	0.90	--	2.10	-1.89	
						-31.02	
					Net Qty	272.56	
	Toilet block						
	<u>Inside</u> <u>plastering</u>						
	Bath/toilet	6	7.60	-	2.40	109.44	


	Corridor		1	36.80	-	2.40	88.32	
							197.76	
	<u>Deduction:-</u>							
	D		-3	0.90	-	2.10	-5.67	
	D1		-6	0.75	-	2.10	-9.45	
	W		-1	1.98	-	1.20	-2.38	
	V1		-6	0.75	-	0.60	-2.70	
							-20.20	
		Net Qty =		197.76	-	-20.20	177.56	
	<u>Inside plastering</u>							
	Bath/toilet		8	5.50	-	2.40	105.60	
	do		2	4.30	-	2.40	20.64	
	Corridor		1	20.60	-	2.40	49.44	
							175.68	
	<u>Deduction:-</u>							
	D		-1	0.90	-	2.10	-1.89	
	D1		-10	0.75	-	2.10	-15.75	
	V		-13	0.75	-	0.60	-5.85	
	W		-1	1.20	-	0.90	-1.08	
							-24.57	
		Net Qty =		175.68	-	-24.57	151.11	
	<u>Inside plastering</u>							
	Bath/toilet		20	7.80	-	2.40	374.40	
	Corridor		1	33.80	-	2.40	81.12	
							455.52	
	<u>Deduction:-</u>							
	D		-1	0.90	-	2.10	-1.89	
	D1		-20	0.75	-	2.10	-31.50	
	V		-20	0.75	-	0.60	-9.00	
							-42.39	
		Net Qty =		455.52	-	-42.39	413.13	
				Total Qty Work Done			1014.36	
Qty payable in this Upto 125%							340.75	sqm
Qty payable in this Above 125%							673.61	sqm

For S.K.S. INFRASTRUCTURES PVT. LTD.


Contractor Representative
Managing Director


Assistant Engineer
Project -RR Nagar Division
BBMP


Consultants Representative


Asst. Executive Engineer
Project -RR Nagar Division
BBMP

BRUHAT BANGALORE MAHANAGARA PALIKE							
NAME OF THE WORK: Modified of Additional works to construction of shuttle cock Ground In Ward No 17 RR Nagar constituency							
Measurement Sheet							
First and Final							
Item No:	26						
Item Name:	For External Plastering:- Providing 18mm thick cement plaster in single coat with cement mortar 1:4, to brick masonry including rounding off corners wherever required smooth rendering: Providing and removing scaffolding, including cost of materials, labour, curing complete as per specifications.As Per Direction of Engineer Incharge.						
	CHAINAGE	NO	L	B	D	QTY	REMARKS
	Land Mark		(m)	(m)	(m)		
	Toilets	1	12.80		3.60	46.08	
		2	4.55		3.60	32.76	
		2	12.80		0.75	19.20	
		2	4.55		0.75	6.83	
	Parapet wall	4	12.95		1.00	51.80	
		4	4.57		1.00	18.28	
	Storage tank room	4	2.50		2.14	21.40	
		4	2.10		2.14	17.98	
		2	10.00		0.80	16.00	
						230.32	
	Toilet block						
	<u>Outside plastering</u>						
	Outer length	1	38.40		2.40	92.16	
	<u>Deduction:-</u>						
	D	1	0.90	-	2.10	1.89	
	W	1	1.98	-	1.20	2.38	
	V1	6	0.75	-	0.60	2.70	
						6.97	
			6.97	/	2.00	3.48	
		Net Qty =		92.16	-	3.48	88.68
	<u>Outside plastering</u>						
	Outer length	1	25.80		2.40	61.92	
	Toilet	1	4.50		2.40	10.80	
						72.72	
	<u>Deduction:-</u>						
	D	1	0.90	-	2.10	1.89	
	V	13	0.75	-	0.60	5.85	
	W	1	1.20	-	0.90	1.08	
						8.82	
			8.82	/	2.00	4.41	
		Net Qty =		72.72	-	4.41	68.31
	<u>Outside plastering</u>						
	Outer length	1	42.20		2.40	101.28	
	<u>Deduction:-</u>						
	D	1	0.90	-	2.10	1.89	
	V	20	0.75	-	0.60	9.00	
						10.89	

			10.89	/	2.00	5.45	
		Net Qty =	101.28	-	5.45	95.84	
			Total Qty Work Done			483.14	
			Qty payable in this Upto 125%			287.90	sqm
			Qty payable in this Above 125%			195.24	sqm

For S.K.S. INFRASTRUCTURES PVT. LTD.

[Signature]

Contractor Representative

Managing Director



Consultants Representative

[Signature]

Assistant Engineer

Project -RR Nagar Division
BBMP

[Signature]

Asst. Executive Engineer

Project -RR Nagar Division
BBMP

BRUHAT BANGALORE MAHANAGARA PALIKE							
NAME OF THE WORK: Modified of Additional works to construction of shuttle cock Ground In Ward No 17 RR Nagar constituency							
Measurement Sheet							
First and Final							
Item No:	27						
Item Name:	Providing rough plastering 15mm thick in single coat with cement mortor 1:4, to brick masonry for base of dadooing works with sand of approved quality, providing and removing scaffolding, including cost of materials, labour, curing complete as per specifications.As Per Direction of Engineer Incharge						
	CHAINAGE	NO	L	B	D	QTY	REMARKS
	Land Mark		(m)	(m)	(m)		
	For dadooing						
	Gents Toilet						
		1	2.50	--	2.10	5.25	
		1	4.50	--	2.10	9.45	
		1	1.15	--	2.10	2.42	
		1	2.40	--	2.10	5.04	
		1	1.30	--	2.10	2.73	
		1	2.00	--	2.10	4.20	
	Toilet						
		2	2.15	--	2.10	9.03	
		2	2.35	--	2.10	9.87	
	Ladies Toilet	12	1.06	--	2.10	26.71	
		2	0.76	--	2.10	3.20	
		1	2.72	--	2.10	5.71	
		8	2.15	--	2.10	36.12	
		2	2.43		2.10	10.21	
						129.94	
	Deduction						
	D2	2	0.75	--	2.10	3.15	
	V	2	0.90	--	0.60	1.08	
		1	1.50		0.60	0.90	
	V1	2	0.90		0.60	1.08	
	D1	1	1.20	--	2.10	2.52	
	D	1	0.70	--	2.10	1.47	
		4	0.75	--	2.10	6.30	
		1	0.90	--	2.10	1.89	

							18.39	
						Net Qty	111.55	
			Total Qty Work Done				111.55	SQM
			Qty payable in this Bill				111.55	SQM

For S.K.S. INFRASTRUCTURES PVT. LTD.

[Signature]
Contractor Representative
Managing Director



Consultants Representative

[Signature]
Assistant Engineer
Project -RR Nagar Division
BBMP

[Signature]
Asst. Executive Engineer
Project -RR Nagar Division
BBMP
